



Education Center Reuse Community Newsletter (Sept 2019)

This is the September 2019 update on the status and progress of construction for the project. All monthly updates are posted to the project website and can be accessed via the following link:

<https://www.apsva.us/education-center-reuse/>

The interior demolition package has completed on schedule! Concurrent with interior demolition the design is continuing. Full construction is scheduled to begin in January 2020.

This will be the last update published until construction activities resume in 2020.

As a reminder the project's community liaison is Robin Hodges, Arlington Public Schools, Design and Construction Project Manager who can be reached at (703) 872-9175 or robin.hodges@apsva.us.

Jeffrey D. Chambers, NCARB, AIA, Director of Design & Construction



Completed and ongoing tasks:

- 1st – 4th, and Ground Floor demolition and abatement activities
- Planetarium temporary closing to occur November 26, 2019
- Various design survey components are ongoing

Process related activities:


- Design survey activities will continue between 7am to 5pm on weekdays as needed on site.
- The submission of the 65% Complete Design Drawings occurred and concurrent reviews between all parties are complete
- The submission of the 95% Design Drawings on schedule for review in November – December 2019
- Contractor parking assigned to the previous Ed Center patron parking spaces.

Progress Photos:

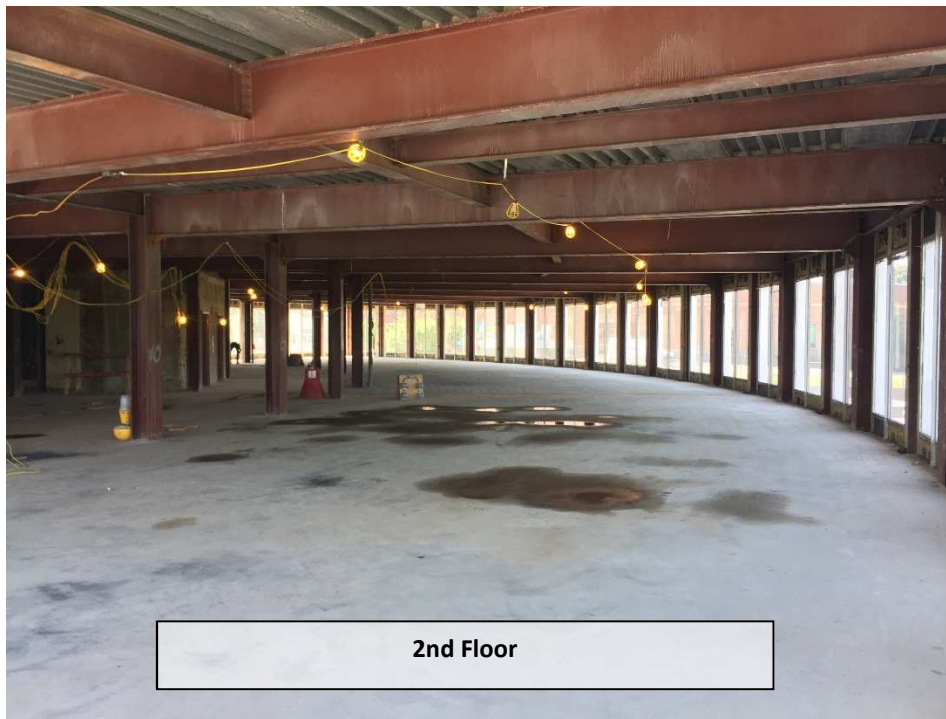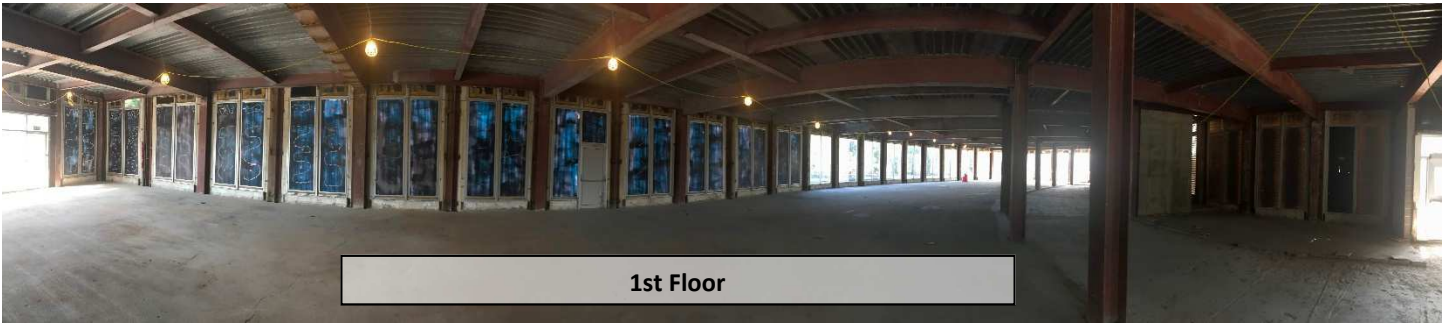




3rd Floor

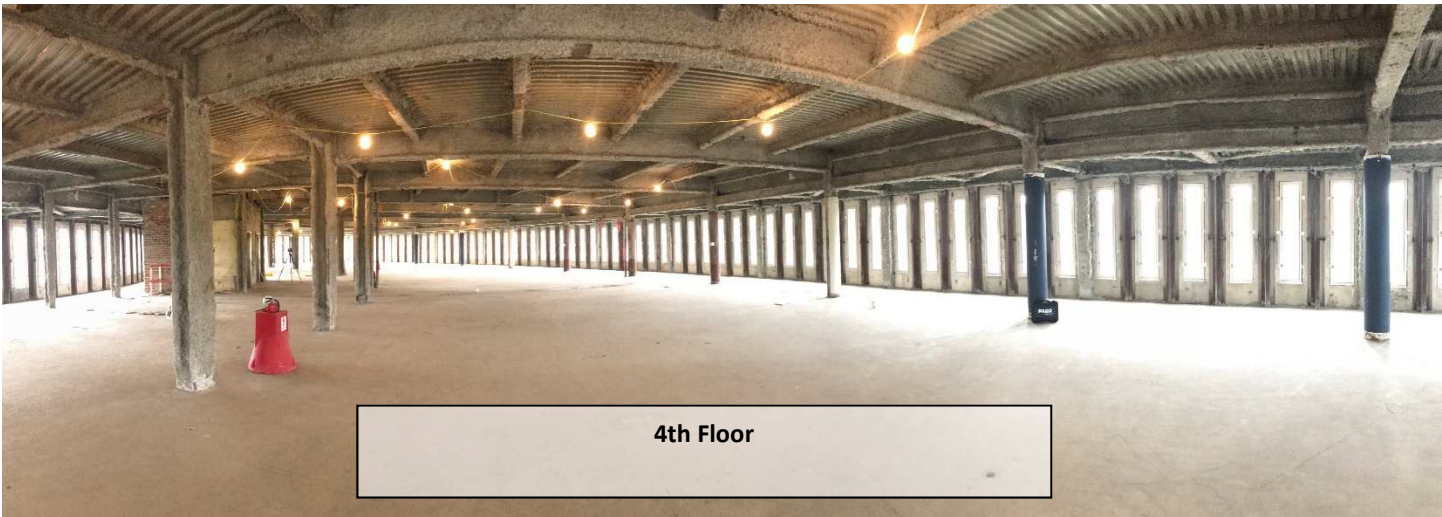

4th Floor

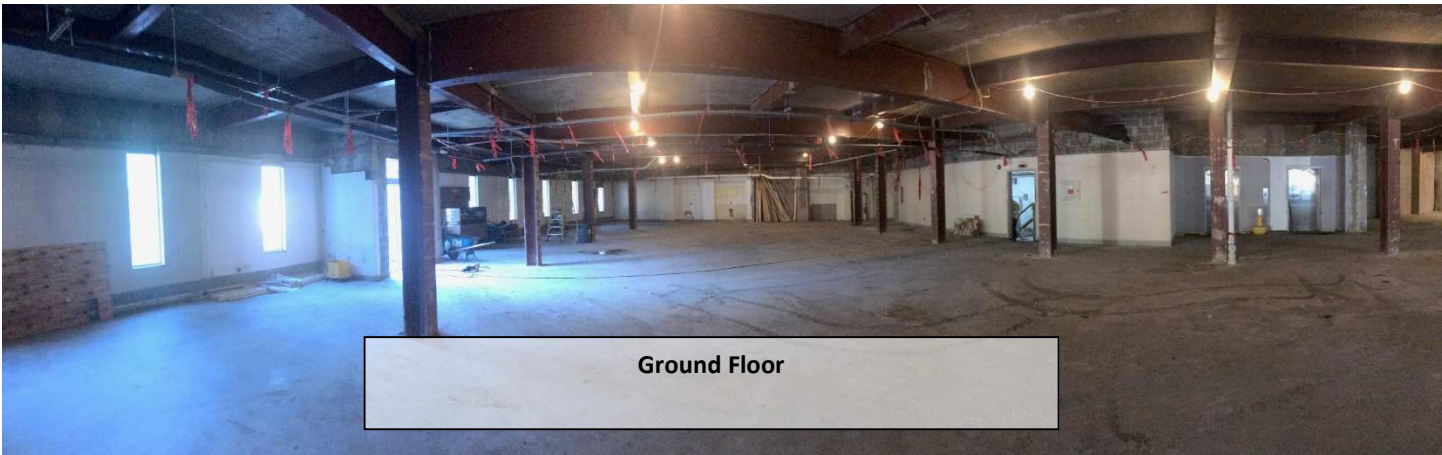

Ground Floor
